



Shaler Area School District

## SCOTT PRIMARY SCHOOL



March 29, 2018



**Massaro**  
CM SERVICES, LLC



# Main Entry



**Massaro**  
CM SERVICES, LLC





# Metal Roofing has Begun



**Massaro**  
CM SERVICES, LLC





# Gym Floor Prep



**Massaro**  
CM SERVICES, LLC





# Stage @ Gym





# Interior Painting Continues – First Floor



**Massaro**  
CM SERVICES, LLC





# Interior Painting Continues – Ground Floor



**Massaro**  
CM SERVICES, LLC



# Ground Floor Color Scheme







# Ground Floor Color Scheme



**Massaro**  
CM SERVICES, LLC



# Drywall @ Library Continues



**Massaro**  
CM SERVICES, LLC





# Ceiling Grid @ Corridors Continues



**Massaro**  
CM SERVICES, LLC



# Ceiling Grid @ Classrooms Continues







# Lockers Are Being Installed





# Ground Floor CMU Walls



**Massaro**  
CM SERVICES, LLC





# North Elevation View

March 29, 2018



**Massaro**  
CM SERVICES, LLC



# South Elevation View

March 29, 2018




**Massaro**  
CM SERVICES, LLC





# Finish Schedule

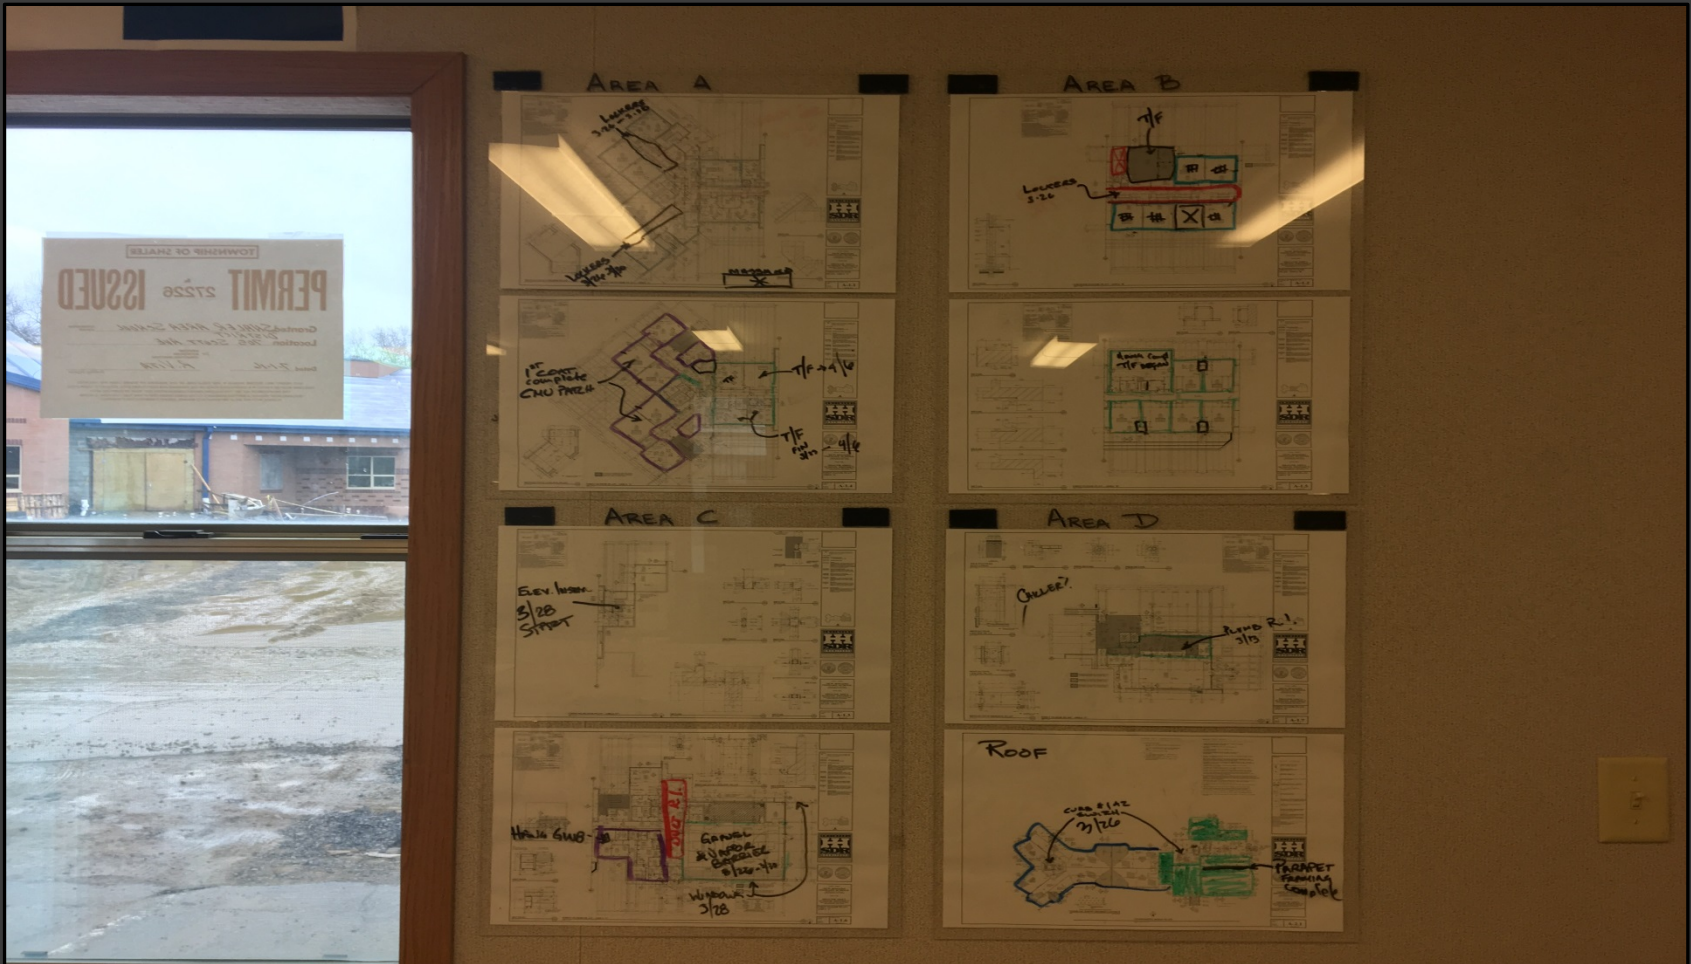



# Pull Planning

## Week of March 26, 2018

PRIME	MON.	TUES.	WED.	THUR.	FRI.	WEEKLY GOALS WEEK ENDING 3.23.18 <sup>12</sup> / <sub>21</sub>
A-13 SARGENT 3	<ul style="list-style-type: none"> <li>- Lights in GOLF</li> <li>- R.I. w/ Dandelings</li> </ul>	<ul style="list-style-type: none"> <li>- VAY'S in Gym</li> <li>- R.I. in C-Admin</li> </ul>		<ul style="list-style-type: none"> <li>-&gt;</li> <li>-&gt;</li> </ul>		<ul style="list-style-type: none"> <li>- Classroom Doors Complete GR FL</li> <li>- A/B</li> <li>- Fan Wire for BLEN</li> </ul>
NELLO	<ul style="list-style-type: none"> <li>- PA Booth - R.I. #12 Sound</li> <li>- to sound standing Gears</li> <li>- The - Floor w/ PTE RAILINGS</li> <li>- GROUNDING W/ TIE</li> <li>- LOCKERS GR FL</li> <li>- EXTERIOR STEP FORMS</li> <li>- Scaffolding</li> <li>- Gym EROVEL - P. R. R. R.</li> </ul>	<ul style="list-style-type: none"> <li>- Gym VAY'S BARRIER</li> </ul>	<ul style="list-style-type: none"> <li>- WINDOWS</li> <li>- OTIS ON SITE</li> </ul>	<ul style="list-style-type: none"> <li>-&gt;</li> <li>-&gt;</li> <li>-&gt;</li> <li>-&gt;</li> <li>-&gt;</li> <li>-&gt;</li> </ul>		<ul style="list-style-type: none"> <li>- VAY'S BARRIER in Gym</li> <li>- BLEN ELEVATOR INSTALL</li> <li>- RAILING W/ WOOD VERTICAL</li> <li>- WOODING C/D COMPLETE</li> <li>- TEMP HEAT C/D</li> <li>- GR FL LOCKERS INSTALL</li> </ul>
RAM 12. CAMP 2 FL.	<ul style="list-style-type: none"> <li>- FIN. HANG IN LIBRARY</li> <li>- T/P in AREA B 1<sup>ST</sup> FL</li> <li>- T/P BENCH ROOM CEILING</li> <li>- BUNGARDS C/D</li> </ul>			<ul style="list-style-type: none"> <li>- SCAFFOLDING IN STAIR</li> <li>- S2</li> </ul>		<ul style="list-style-type: none"> <li>- FIN. HANG LIBRARY</li> <li>- FRAME BUNGARDS C/D</li> <li>- SCAFFOLD STAIRS S2</li> </ul>
HARRIS 3/5	<ul style="list-style-type: none"> <li>- WOOD WEST Gym Wall</li> <li>- ENTRANCE CANOPIES</li> </ul>					<ul style="list-style-type: none"> <li>- ENTRANCE CANOPIES COMPLETE</li> <li>- MOD. ELEV CANOPIES COMPLETE</li> <li>- WOOD WEST Gym Wall Complete</li> </ul>
VABEL 3	<ul style="list-style-type: none"> <li>- VAY'S LABELS GR FL</li> <li>- SEAL WALL PENETRATIONS</li> </ul>		<ul style="list-style-type: none"> <li>- SPRINKLER HEADS</li> </ul>			<ul style="list-style-type: none"> <li>- SPRINKLER HEADS GR FL</li> <li>- COMPLETE IN CLASS ROOMS</li> <li>- SPRINKLER HEADS COTTAGES</li> <li>- STREET</li> </ul>
HRANEC 4	<ul style="list-style-type: none"> <li>- ELEV IN C RESTROOMS</li> <li>- DUCT DELIVERIES</li> <li>- GATE DIFFUSERS</li> <li>- AREA D DUCT</li> </ul>					
EAST WEST +1	<ul style="list-style-type: none"> <li>- FIN #1 #2 CURB SWIM</li> </ul>	<ul style="list-style-type: none"> <li>- VAY'S in C</li> </ul>				<ul style="list-style-type: none"> <li>- STAIRS #1 #2 CUBES</li> <li>- VAY FINAL CONN. ADMIN</li> <li>- SD 700 COMPLETE</li> </ul>







# NEW PRIMARY SCHOOL ON SCOTT AVE.

Scheduled Work for Upcoming Weeks

- Continue MEP Systems
- Interior CMU
- Interior Drywall
- Interior Ceramic
- Interior Painting
- Roofing

