



Shaler Area School District


## SCOTT PRIMARY SCHOOL



Project Progress  
November 17, 2017



# Roof Decking


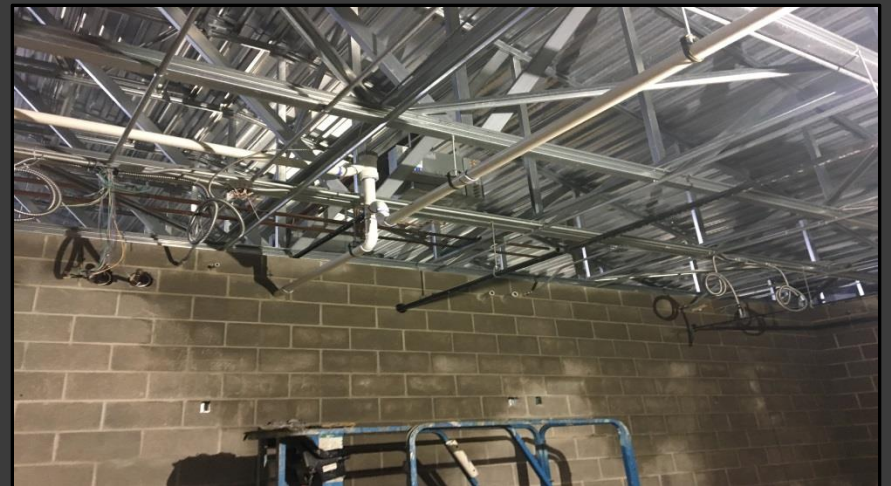


**Massaro**  
CM SERVICES, LLC





# MEP Work Continues

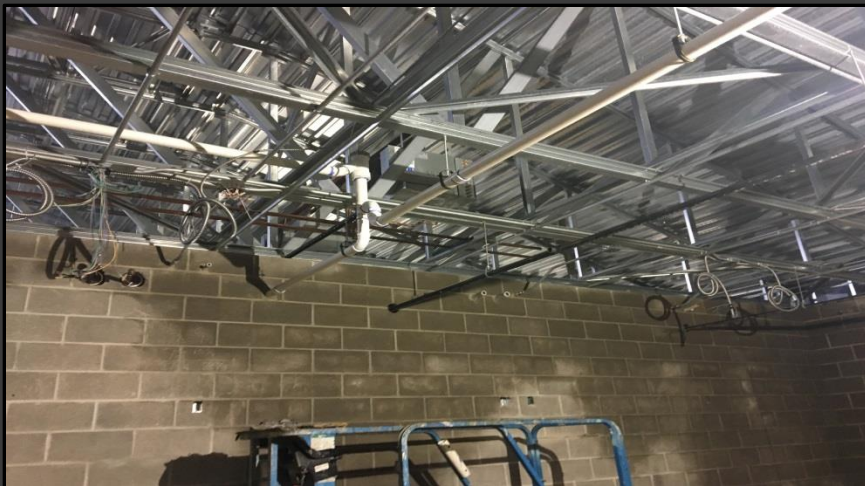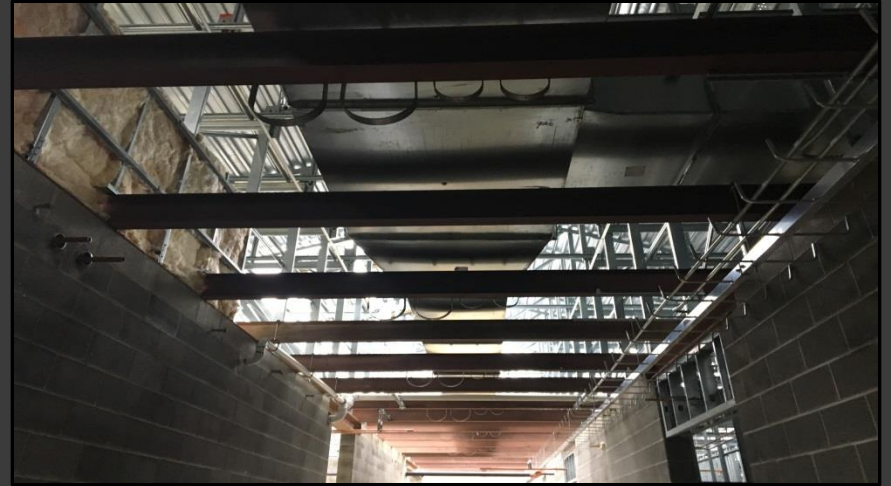

**Massaro**  
CM SERVICES, LLC





# MEP Work Continues



**Massaro**  
CM SERVICES, LLC





# Masonry Areas C & D



**Massaro**  
CM SERVICES, LLC





# Masonry Areas C & D



**Massaro**  
CM SERVICES, LLC





# Gymnasium





# Exterior Masonry @ C & D



**Massaro**  
CM SERVICES, LLC





# North Elevation View

November 17, 2017



**Massaro**  
CM SERVICES, LLC





# South Elevation View

November 17, 2017



**Massaro**  
CM SERVICES, LLC





# Pull Planning

## Week of November 13, 2017

PRIME	MON.	TUES.	WED.	THUR.	FRI.	S.O.G.
A-1	<ul style="list-style-type: none"> <li>CMU R1 - C/D</li> <li>Cast 1st Fl Area B</li> <li>Leaving Wire in Hands</li> <li>Gr Fl Area B</li> </ul>	<ul style="list-style-type: none"> <li>CMU R1 Area C/D</li> <li>Cast Tray 1st Fl Area B</li> <li>Leaving Wire in Hands</li> <li>Gr Fl Area B</li> </ul>				<ul style="list-style-type: none"> <li>Cast Tray Area B 1st Fl</li> </ul>
R & B	OFF SITE	<ul style="list-style-type: none"> <li>Hoar Lot</li> <li>Cast Basin North Lot</li> <li>Ret. Tank #1 Caps</li> </ul>	<ul style="list-style-type: none"> <li>Cast Basin South North Lot</li> <li>Ret. Tank #1 Caps</li> </ul>	<ul style="list-style-type: none"> <li>Cast Basin South North Lot</li> <li>Ret. Tank #1 Caps</li> </ul>	<ul style="list-style-type: none"> <li>Cast Basin South North Lot</li> <li>Ret. Tank #1 Caps</li> </ul>	<ul style="list-style-type: none"> <li>Begin Ret. Tank #1 Caps</li> </ul>
HARRIS	<ul style="list-style-type: none"> <li>CMU STRIP 3/ELEVATOR</li> <li>South Area D Brick</li> <li>Brick West Gym Wall</li> <li>Area C/D Walls</li> </ul>	<ul style="list-style-type: none"> <li>CMU STRIP 3/ELEVATOR</li> <li>South Area D (Leaving Wire) Brick</li> <li>West Gym Wall Brick</li> <li>Area C/D CMU Bearing Walls</li> <li>Chiller Base Wall Dams</li> <li>North Area C Walls</li> </ul>	<ul style="list-style-type: none"> <li>Strip 3 CMU Complete</li> <li>South Area D (Leaving Wire) Brick</li> <li>West Gym Wall Brick</li> <li>Area C/D CMU Bearing Walls</li> <li>Exterior Walls</li> </ul>	<ul style="list-style-type: none"> <li>South Area D Brick</li> <li>West Gym Wall Brick</li> <li>C/D CMU Bearing Walls</li> </ul>	<ul style="list-style-type: none"> <li>South Area D Brick</li> <li>West Gym Wall Brick</li> <li>C/D CMU Bearing Walls</li> </ul>	<ul style="list-style-type: none"> <li>Complete Strip 3/ELEVATOR CMU Walls Complete</li> <li>END AREA C NORTH ADMIN WALL</li> <li>Chiller Wall Brick Complete</li> </ul>
VELLO	<ul style="list-style-type: none"> <li>RAM: DORMERS</li> <li>INT. FRAMING A/B</li> <li>INT. BLOCKING A/B</li> <li>Beam Cops West Lot</li> <li>Dormer/Louver Install</li> <li>A/B Roof Decking</li> </ul>	<ul style="list-style-type: none"> <li>INT. BLOCKING A/B</li> <li>Beam Cops West Lot</li> <li>Dormer/Louver Install</li> <li>Roof Decking A/B</li> </ul>	<ul style="list-style-type: none"> <li>INT. BLOCKING A/B</li> <li>Roofing Area A</li> <li>Beam Cops West Lot</li> <li>Beam Cops C S.O.G.</li> <li>Roof Decking A/B</li> </ul>	<ul style="list-style-type: none"> <li>INT. BLOCKING A/B</li> <li>LOUVER INSTALL</li> <li>Roofing Area A</li> <li>Beam Cops S.O.G. #2</li> <li>Beam Cops Area A</li> <li>Beam Cops Area A</li> <li>Beam Cops Area A</li> </ul>	<ul style="list-style-type: none"> <li>INT. BLOCKING A/B</li> <li>LOUVER INSTALL</li> <li>Roofing Area A</li> <li>Beam Cops North Area A</li> <li>Beam Cops Area A</li> </ul>	<ul style="list-style-type: none"> <li>Beam Cops Area C S.O.G.</li> <li>Beam Cops Area A Franco</li> <li>Beam Cops S.O.G. South Area A</li> <li>Beam Cops Area A</li> <li>Complete Roof Decking A/B</li> </ul>
VRABEL	<ul style="list-style-type: none"> <li>SPRINKLER ARM DUCTS</li> <li>Area C Restroom R1</li> </ul>	<ul style="list-style-type: none"> <li>SPRINKLER ARM DUCTS</li> <li>Area C Restroom R1</li> </ul>	<ul style="list-style-type: none"> <li>Area C Restroom R1</li> </ul>	<ul style="list-style-type: none"> <li>Area C Restroom R1</li> </ul>	<ul style="list-style-type: none"> <li>Area C Restroom R1</li> </ul>	<ul style="list-style-type: none"> <li>Begin CHASE INSTALL AREA C Restrooms</li> </ul>
HRANEK	1st Fl Duct A/B	1st Fl Duct A/B	OFF SITE	1st Fl Duct A/B	1st Fl Duct A/B	
EAST WEST	VAN BOXES IN AREA A	VAN'S AREA A 1st Fl	Hot Water Main 1st Fl B	Hot Water Main 1st Fl B	Hot Water Main 1st Fl B	Begin Hot Water Pipe in Area B 1st Fl







# NEW PRIMARY SCHOOL ON SCOTT AVE.

Scheduled Work for Upcoming Weeks

- Continue Louvers & Windows
- Continue MEP Systems
- West Parking Lot
- Metal Decking on Area B
- Steel Joists Area C
- Interior Metal Framing
- Interior/Exterior CMU @ Area C & D



**Massaro**  
CM SERVICES, LLC
