



Shaler Area School District

SCOTT PRIMARY SCHOOL



Project Progress
January 19, 2018



MEP's Continue



Massaro
CM SERVICES, LLC




MEP's Continue



Massaro
CM SERVICES, LLC



Area C - Cafeteria

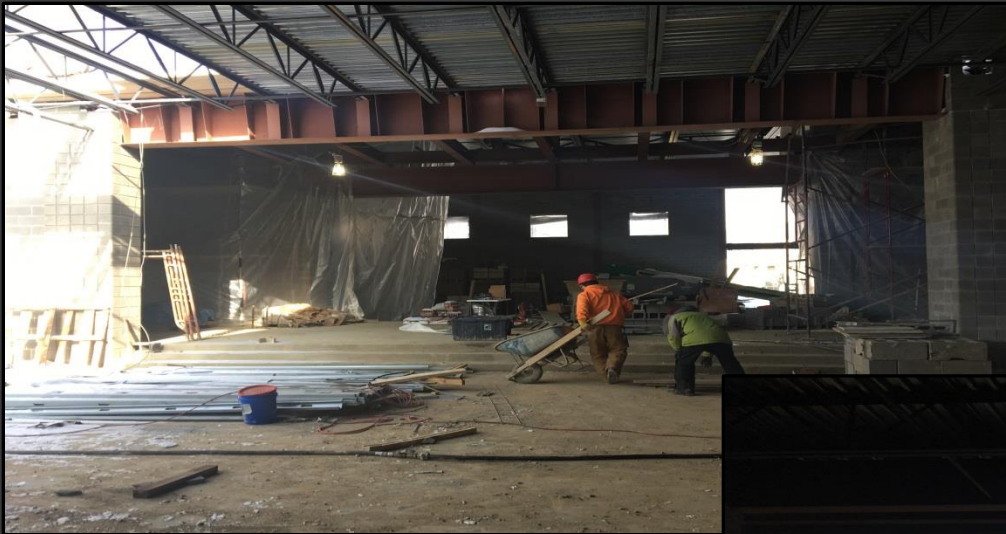



Canopy @ Main Entrance



Massaro
CM SERVICES, LLC



Exterior Masonry



Massaro
CM SERVICES, LLC



Interior Framing



Massaro
CM SERVICES, LLC



Library



Massaro
CM SERVICES, LLC



North Elevation View

January 19, 2018



Massaro
CM SERVICES, LLC



South Elevation View

January 19, 2015



Massaro
CM SERVICES, LLC



Pull Planning

Week of January 15, 2018

PRIME	MON.	TUES.	WED.	THUR.	FRI.	S.O.G.
A-1	• Devices in B.R.		Admin Panels			• Devices in Boiler Room Admin Panels
NELLO	• TENSING • EXTERIOR STAIRS CEILING • EXTERIOR INTERIOR PLACING		• PA Roofing A • STEEL PAN STAIRS	• PA Roofing A →	• PA Roofing A+C	• AREA C DECKING COMPLETE • AREA C/D STEEL DETAILING
RAM	• INSULATING PERIM A/B • TRUSS MODS	• ADMIN FRAMING • TRUSS MODS	• ADMIN FRAMING • PERISCO DUNDLES • TRUSS MODS	• PERISCO DUNDLES • TRUSS MODS	• ADMIN FRAMING • PERISCO DUNDLES • TRUSS MODS	• BEGIN ADMIN FRAMING • TRUSS MODIFICATIONS A/B • INSULATE PERIM A/B • DEMOLISH PERISCO A/B EXTERIOR
HARRIS	• BRICK WALK WALL GYM • CMU STAIR 2 • VINCE CMU INTERIOR A/B	• WASH DOWN ADMIN • SCARFOLD D ENTRANCE • CMU MEZZ WALKS	→ • CMU @ D ENTRANCE • STAIR 1 CMU	• WASH DOWN KITCHEN	→ → → →	• MESSAGING WALK • EXTERIOR WALK @ D ENTRANCE • WASH BRICK C ADMIN ROOF • WASH BRICK KITCHEN ROOF • BRICK EAST WALL OF GYM (STAIRS)
VRABEL	OFF SITE			→	RI C/D ?	• BEGIN RI C/D
HRANEC	• HANG DUCT IN GARAGE B/A	→	• BIG DUCT COMPLETE	• DUCT TAPS B/A	• DUCT TAPS B/A	• BIG DUCT & A/B COMPLETE • BEGIN TAPS
EAST WEST	• CONTROL A/B	• CONTROL A/B	• HOT WATER MAINS B/A • CONTROL A/B	• CONTROL A/B	→ • CONTROL A/B	• BEGIN HOT WATER MAINS





NEW PRIMARY SCHOOL ON SCOTT AVE.

Scheduled Work for Upcoming Weeks

- Continue MEP Systems
- Steel Joists Area C
- Metal Decking on Area C
- Interior Metal Framing
- Interior/Exterior CMU @ Area C & D
- Roofing

