



Shaler Area School District


SCOTT PRIMARY SCHOOL



Project Progress
November 03, 2017



Roof Decking

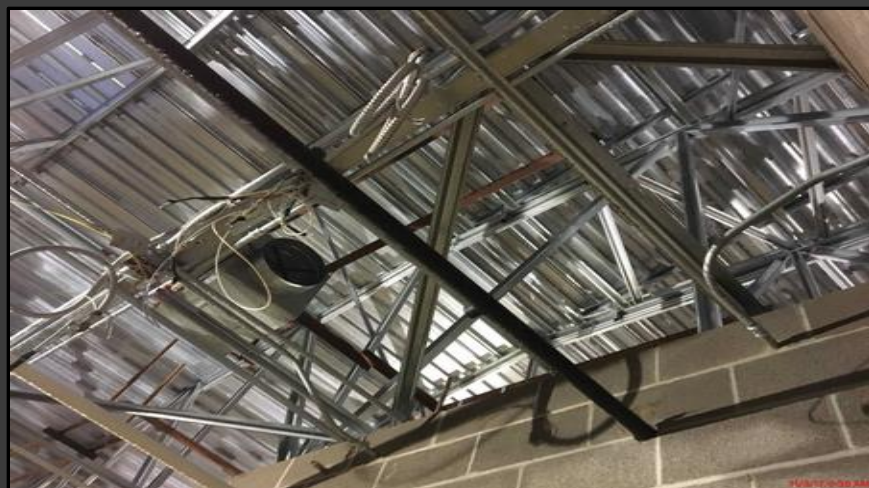

Massaro
CM SERVICES, LLC



Exterior Masonry



Massaro
CM SERVICES, LLC



MEP work in Areas A & B



Massaro
CM SERVICES, LLC



Masonry Areas C & D





Masonry Areas C & D





Masonry @ Gym





North Elevation View

November 03, 2017



Massaro
CM SERVICES, LLC



Pull Planning

Week of October 30, 2017

PRIME	MON.	TUES.	WED.	THUR.	FRI.	S.O.G.
A-1	-FA ON 1 ST F A+B -TRANSFORMER -GE F-A/B POWER RI	Fix Alarm RI 1 ST F A+B GE F A/B POWER RI	Fix Alarm RI 1 ST F A+B 1 ST F B - O.H. CONDUIT	Fix Alarm RI 1 ST F A+B 1 ST F B O.H. CONDUIT	Fix Alarm RI 1 ST F A+B -PEEL POWER ? 1 ST F B O.H. CONDUIT	
R&B	DEMO SIDEWALK	DEMO SIDEWALK	DEMO SIDEWALK RAIN LEADERS SOUTH A	WEST LOT	WEST LOT	-Begin Sidewalk Demo
HARRIS	-South BRICK -South AREA D BRICK -BRICK West Gym Wall -AREA C/D WALLS	-South BRICK COMPLETE -South AREA D (Common Area) BRICK -West Gym Wall BRICK -AREA C/D CONCRETE BRICK WALLS -ELEVATOR SHAFT WALLS	-South BRICK West Gym Wall -South AREA D (Common Area) BRICK -West Gym Wall BRICK -AREA C/D CONCRETE BRICK WALLS -ELEVATOR SHAFT WALLS	-South BRICK West Gym Wall -South AREA D (Common Area) BRICK -West Gym Wall BRICK -ELEVATOR SHAFT WALLS -C/D CONCRETE BRICK WALLS	-South BRICK West Gym Wall -South AREA D (Common Area) BRICK -West Gym Wall BRICK -ELEVATOR SHAFT WALLS -C/D CONCRETE BRICK WALLS	-South BRICK West Gym Wall -South AREA D (Common Area) BRICK -West Gym Wall BRICK -ELEVATOR SHAFT WALLS -C/D CONCRETE BRICK WALLS
NELO	-RAM: SOUTH FORMING AREA D -SOUTH FORMING AREA D -BRICKING CUES WEST LOT -ROOF DECKING AREA A	-RAM: SOUTH FORMING AREA D -SOUTH FORMING AREA D -BRICKING CUES WEST LOT -ROOF DECKING AREA A	-RAM: SOUTH FORMING AREA D -SOUTH FORMING AREA D -BRICKING CUES WEST LOT -ROOF DECKING AREA A	-RAM: SOUTH FORMING AREA D -SOUTH FORMING AREA D -BRICKING CUES WEST LOT -ROOF DECKING AREA A	-RAM: SOUTH FORMING AREA D -SOUTH FORMING AREA D -BRICKING CUES WEST LOT -ROOF DECKING AREA A	-RAM: SOUTH FORMING AREA D -SOUTH FORMING AREA D -BRICKING CUES WEST LOT -ROOF DECKING AREA A
VRABEL	A+B - ARM OVERS	A+B ARM OVERS	- AREA C RESTROOM RI - A/B ARM OVERS	- AREA C RESTROOM RI	OFF SITE	BEGIN AREA C RESTROOM RI
HRANEK	1 ST F A	OFF SITE	1 ST F A DUCT	1 ST F A DUCT	1 ST F A DUCT	-BEGIN AREA A 1 ST F DUCT
EAST WEST	1 ST F A RI ROOF CUES A COMPLETE	1 ST F A RI	-1 ST F A RI	1 ST F A RI TIE IN VAV'S	1 ST F A RI TIE IN VAV'S	-COMPLETE ROOF CUES AREA A -BEGIN VAV TIE IN AREA A 1 ST F.





NEW PRIMARY SCHOOL ON SCOTT AVE.

Scheduled Work for Upcoming Weeks

- Continue Metal Decking @ Roof
- Continue Louvers & Windows
- West Parking Lot
- Metal Decking on Area A
- Interior Metal Framing
- Interior CMU @ Area C



Massaro
CM SERVICES, LLC
